


# SAMPLE { WBS }







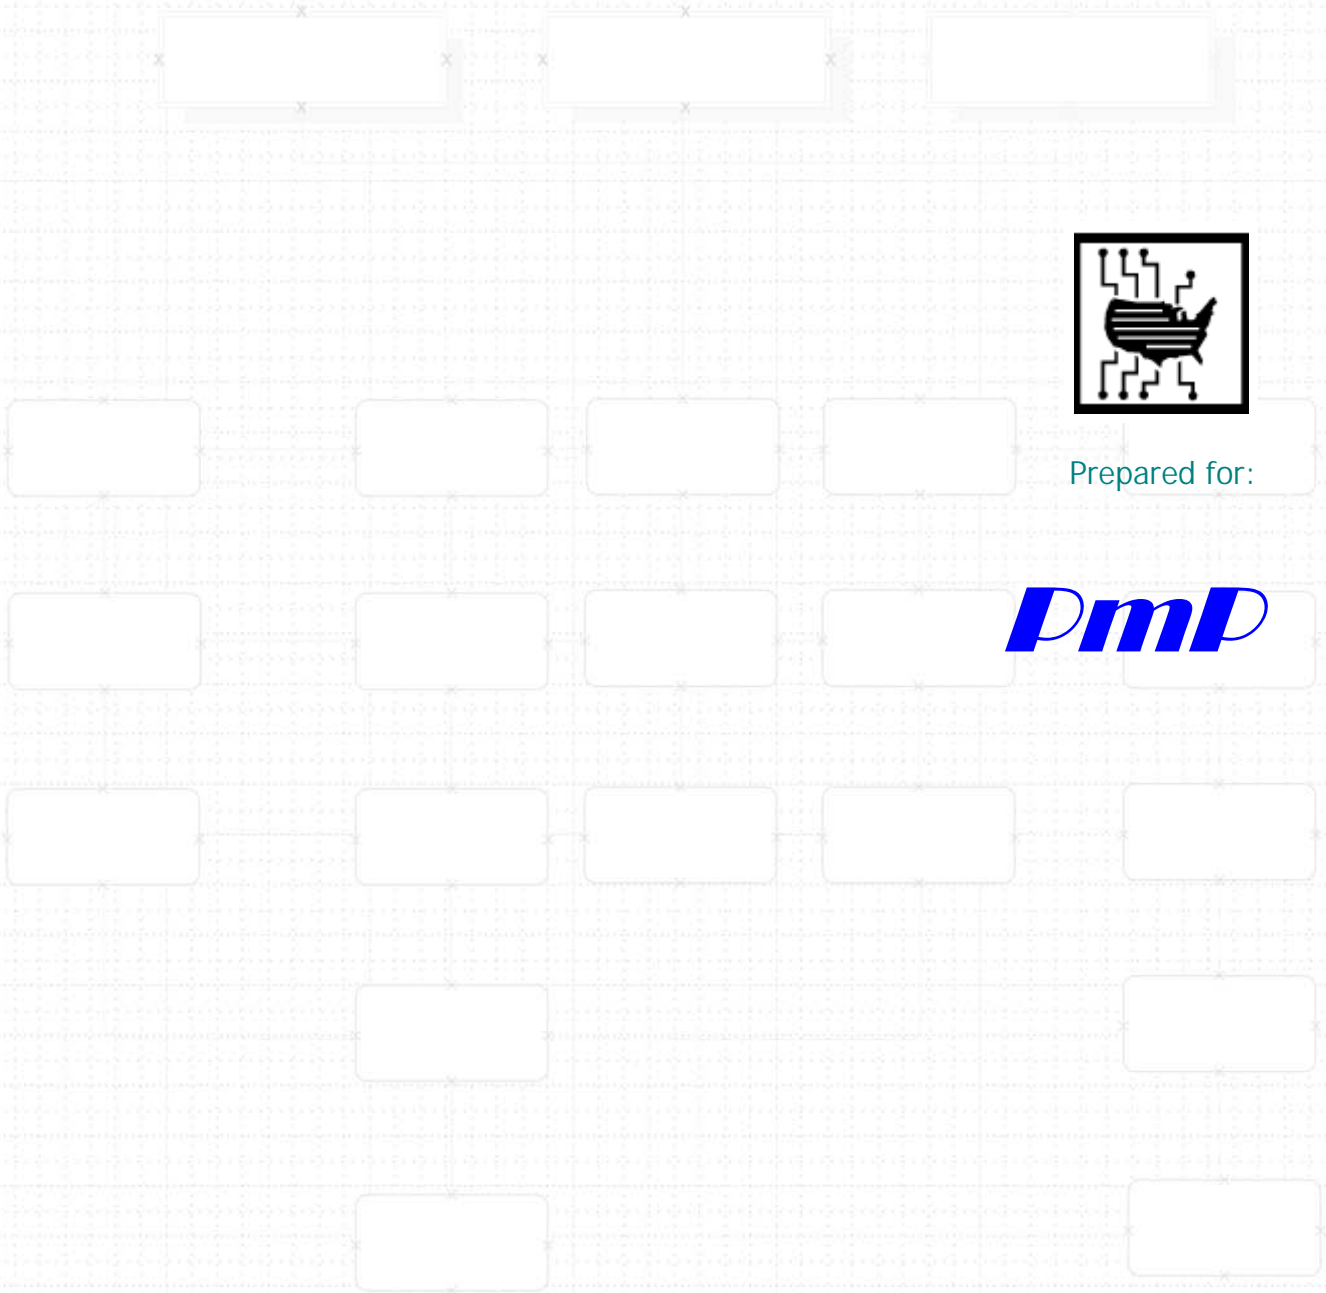


## Work Breakdown Structure












Prepared for:

**Pmp**










ID	Task Name	Cost	Duration	Start	Finish	Predec
0	<b>WBS [PMP - phase 1]</b>	<b>\$ 25,020.00</b>	<b>87 days</b>	<b>Mon 7/30/07</b>	<b>Tue 11/27/07</b>	
1	<b>Milestones</b>	<b>\$ 0.00</b>	<b>82 days</b>	<b>Fri 8/3/07</b>	<b>Tue 11/27/07</b>	
2	Clarified SRS	\$ 0.00	0 hrs	Fri 8/3/07	Fri 8/3/07	10
3	Instant Messenger	\$ 0.00	0 days	Thu 9/20/07	Thu 9/20/07	64
4	Clinic Module	\$ 0.00	0 days	Thu 9/27/07	Thu 9/27/07	51
5	Inventory	\$ 0.00	0 days	Thu 10/25/07	Thu 10/25/07	58
6	Administration	\$ 0.00	0 days	Tue 10/30/07	Tue 10/30/07	72
7	Beta Version	\$ 0.00	0 days	Fri 11/9/07	Fri 11/9/07	75
8	Release	\$ 0.00	0 days	Tue 11/27/07	Tue 11/27/07	73
9	<b>Elaboration</b>	<b>\$ 720.00</b>	<b>5 days</b>	<b>Mon 7/30/07</b>	<b>Fri 8/3/07</b>	
10	Requirements Clarification	\$ 720.00	5 days	Mon 7/30/07	Fri 8/3/07	
11	<b>Implementation</b>	<b>\$ 17,424.00</b>	<b>62 days</b>	<b>Mon 8/6/07</b>	<b>Tue 10/30/07</b>	<b>10</b>
12	<b>Server-side development</b>	<b>\$ 9,936.00</b>	<b>49 days</b>	<b>Mon 8/6/07</b>	<b>Thu 10/11/07</b>	
13	<b>Business Services</b>	<b>\$ 4,896.00</b>	<b>49 days</b>	<b>Mon 8/6/07</b>	<b>Thu 10/11/07</b>	
14	<b>Clinic Management</b>	<b>\$ 1,440.00</b>	<b>10 days</b>	<b>Mon 8/6/07</b>	<b>Fri 8/17/07</b>	
15	Clinic Management	\$ 288.00	2 days	Tue 8/14/07	Wed 8/15/07	
16	Offices Management (including rooms management)	\$ 288.00	2 days	Thu 8/16/07	Fri 8/17/07	
17	Clinic/office holidays Schedule	\$ 432.00	3 days	Mon 8/6/07	Wed 8/8/07	
18	Doctors vacations and working hours schedule	\$ 432.00	3 days	Thu 8/9/07	Mon 8/13/07	
19	<b>Inventory Management</b>	<b>\$ 1,872.00</b>	<b>13 days</b>	<b>Mon 8/20/07</b>	<b>Wed 9/5/07</b>	<b>14</b>
20	Suppliers Management	\$ 288.00	2 days	Tue 9/4/07	Wed 9/5/07	
21	Inventory Items Management	\$ 432.00	3 days	Mon 8/27/07	Wed 8/29/07	
22	Prescriptions Management	\$ 432.00	3 days	Thu 8/30/07	Mon 9/3/07	
23	Delivery Management	\$ 720.00	5 days	Mon 8/20/07	Fri 8/24/07	
24	<b>Appointment Module Improvements</b>	<b>\$ 1,152.00</b>	<b>8 days</b>	<b>Fri 9/28/07</b>	<b>Tue 10/9/07</b>	<b>19</b>
25	"Double Booked" checking	\$ 144.00	1 day	Thu 10/4/07	Thu 10/4/07	
26	Time Slots for appointments types management	\$ 144.00	1 day	Fri 10/5/07	Fri 10/5/07	
27	Private appointments	\$ 288.00	2 days	Fri 9/28/07	Mon 10/1/07	
28	Appointments Filtering by Office	\$ 144.00	1 day	Mon 10/8/07	Mon 10/8/07	
29	Multiple Attendees	\$ 288.00	2 days	Tue 10/2/07	Wed 10/3/07	


Project: WBS [PMP - phase 1] Date: Thu 9/20/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ID	Task Name	Cost	Duration	Start	Finish	Predec
30	Appointment Book Sharing	\$ 144.00	1 day	Tue 10/9/07	Tue 10/9/07	
31	<b>Patient Module Improvements</b>	<b>\$ 144.00</b>	<b>1 day</b>	<b>Wed 10/10/07</b>	<b>Wed 10/10/07</b>	<b>24</b>
32	Copy profile	\$ 144.00	1 day	Wed 10/10/07	Wed 10/10/07	
33	Rooms & Resources	\$ 288.00	2 days	Wed 10/10/07	Thu 10/11/07	
34	<b>Auxiliary Services</b>	<b>\$ 5,040.00</b>	<b>39 days</b>	<b>Mon 8/6/07</b>	<b>Thu 9/27/07</b>	
35	Email Engine	\$ 432.00	3 days	Thu 9/6/07	Mon 9/10/07	19
36	<b>Notification Subsystem</b>	<b>\$ 1,872.00</b>	<b>13 days</b>	<b>Tue 9/11/07</b>	<b>Thu 9/27/07</b>	<b>35</b>
37	Notification Service	\$ 432.00	3 days	Tue 9/11/07	Thu 9/13/07	
38	Notifications about objects state changes	\$ 432.00	3 days	Fri 9/14/07	Tue 9/18/07	
39	Notifications about user's actions	\$ 432.00	3 days	Wed 9/19/07	Fri 9/21/07	
40	Time based notifications	\$ 288.00	2 days	Mon 9/24/07	Tue 9/25/07	
41	Integration with Appointments	\$ 288.00	2 days	Wed 9/26/07	Thu 9/27/07	
42	<b>Instant Messenger</b>	<b>\$ 2,736.00</b>	<b>19 days</b>	<b>Mon 8/6/07</b>	<b>Thu 8/30/07</b>	
43	Messaging Service	\$ 720.00	5 days	Mon 8/6/07	Fri 8/10/07	
44	Contact List (with groups and statuses)	\$ 288.00	2 days	Mon 8/20/07	Tue 8/21/07	
45	Message History management	\$ 288.00	2 days	Wed 8/22/07	Thu 8/23/07	
46	Broadcast messaging	\$ 720.00	5 days	Mon 8/13/07	Fri 8/17/07	
47	Pre-defined messages	\$ 144.00	1 day	Thu 8/30/07	Thu 8/30/07	
48	Settings and Preferences	\$ 288.00	2 days	Fri 8/24/07	Mon 8/27/07	
49	Integration with Appointments	\$ 288.00	2 days	Tue 8/28/07	Wed 8/29/07	
50	<b>Client-side development</b>	<b>\$ 7,488.00</b>	<b>52 days</b>	<b>Mon 8/20/07</b>	<b>Tue 10/30/07</b>	
51	<b>Clinic Management</b>	<b>\$ 2,160.00</b>	<b>29 days</b>	<b>Mon 8/20/07</b>	<b>Thu 9/27/07</b>	<b>14</b>
52	Clinic & Officess	\$ 432.00	3 days	Fri 9/21/07	Tue 9/25/07	
53	Clinic/office holidays schedule	\$ 720.00	5 days	Mon 8/20/07	Fri 8/24/07	
54	Doctors vacations and working hours schedule	\$ 720.00	5 days	Mon 8/27/07	Fri 8/31/07	
55	Integration with Appointments Module	\$ 288.00	2 days	Wed 9/26/07	Thu 9/27/07	
56	<b>Notification</b>	<b>\$ 288.00</b>	<b>2 days</b>	<b>Fri 9/28/07</b>	<b>Mon 10/1/07</b>	<b>64,36</b>
57	Notification Popup Window	\$ 288.00	2 days	Fri 9/28/07	Mon 10/1/07	36
58	<b>Inventory Management</b>	<b>\$ 1,872.00</b>	<b>18 days</b>	<b>Tue 10/2/07</b>	<b>Thu 10/25/07</b>	<b>64,19,!</b>
59	Suppliers management	\$ 288.00	2 days	Wed 10/24/07	Thu 10/25/07	


Project: WBS [PMP - phase 1] Date: Thu 9/20/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ID	Task Name	Cost	Duration	Start	Finish	Predec
60	Inventory Items Management	\$ 432.00	3 days	Thu 10/4/07	Mon 10/8/07	
61	Prescriptions Management	\$ 432.00	3 days	Tue 10/9/07	Thu 10/11/07	
62	Delivery Management	\$ 432.00	3 days	Fri 10/19/07	Tue 10/23/07	
63	Search Function	\$ 288.00	2 days	Tue 10/2/07	Wed 10/3/07	
64	<b>Instant Messenger</b>	<b>\$ 2,016.00</b>	<b>14 days</b>	<b>Mon 9/3/07</b>	<b>Thu 9/20/07</b>	<b>42</b>
65	Contact List View	\$ 288.00	2 days	Tue 9/11/07	Wed 9/12/07	
66	Message Text Dialog	\$ 432.00	3 days	Mon 9/3/07	Wed 9/5/07	
67	Incomming Message Notification	\$ 432.00	3 days	Thu 9/6/07	Mon 9/10/07	
68	History View, Save to File	\$ 288.00	2 days	Thu 9/13/07	Fri 9/14/07	
69	Manage Preferences and Settings	\$ 288.00	2 days	Mon 9/17/07	Tue 9/18/07	
70	Integration with Appointments	\$ 288.00	2 days	Wed 9/19/07	Thu 9/20/07	
71	Appointment Module Improvements	\$ 720.00	5 days	Fri 10/12/07	Thu 10/18/07	63,24
72	Administration	\$ 432.00	3 days	Fri 10/26/07	Tue 10/30/07	51,56,!
73	<b>QA, Stabilizing</b>	<b>\$ 3,744.00</b>	<b>32 days</b>	<b>Mon 10/15/07</b>	<b>Tue 11/27/07</b>	
74	QA - Alpha Testing	\$ 2,160.00	15 days	Mon 10/15/07	Fri 11/2/07	11FF+
75	Stabilizing & Improvements	\$ 720.00	5 days	Mon 11/5/07	Fri 11/9/07	74
76	QA - Beta Testing	\$ 864.00	12 days	Mon 11/12/07	Tue 11/27/07	75
77	Project Management	\$ 3,132.00	87 days	Mon 7/30/07	Tue 11/27/07	


Project: WBS [PMP - phase 1] Date: Thu 9/20/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

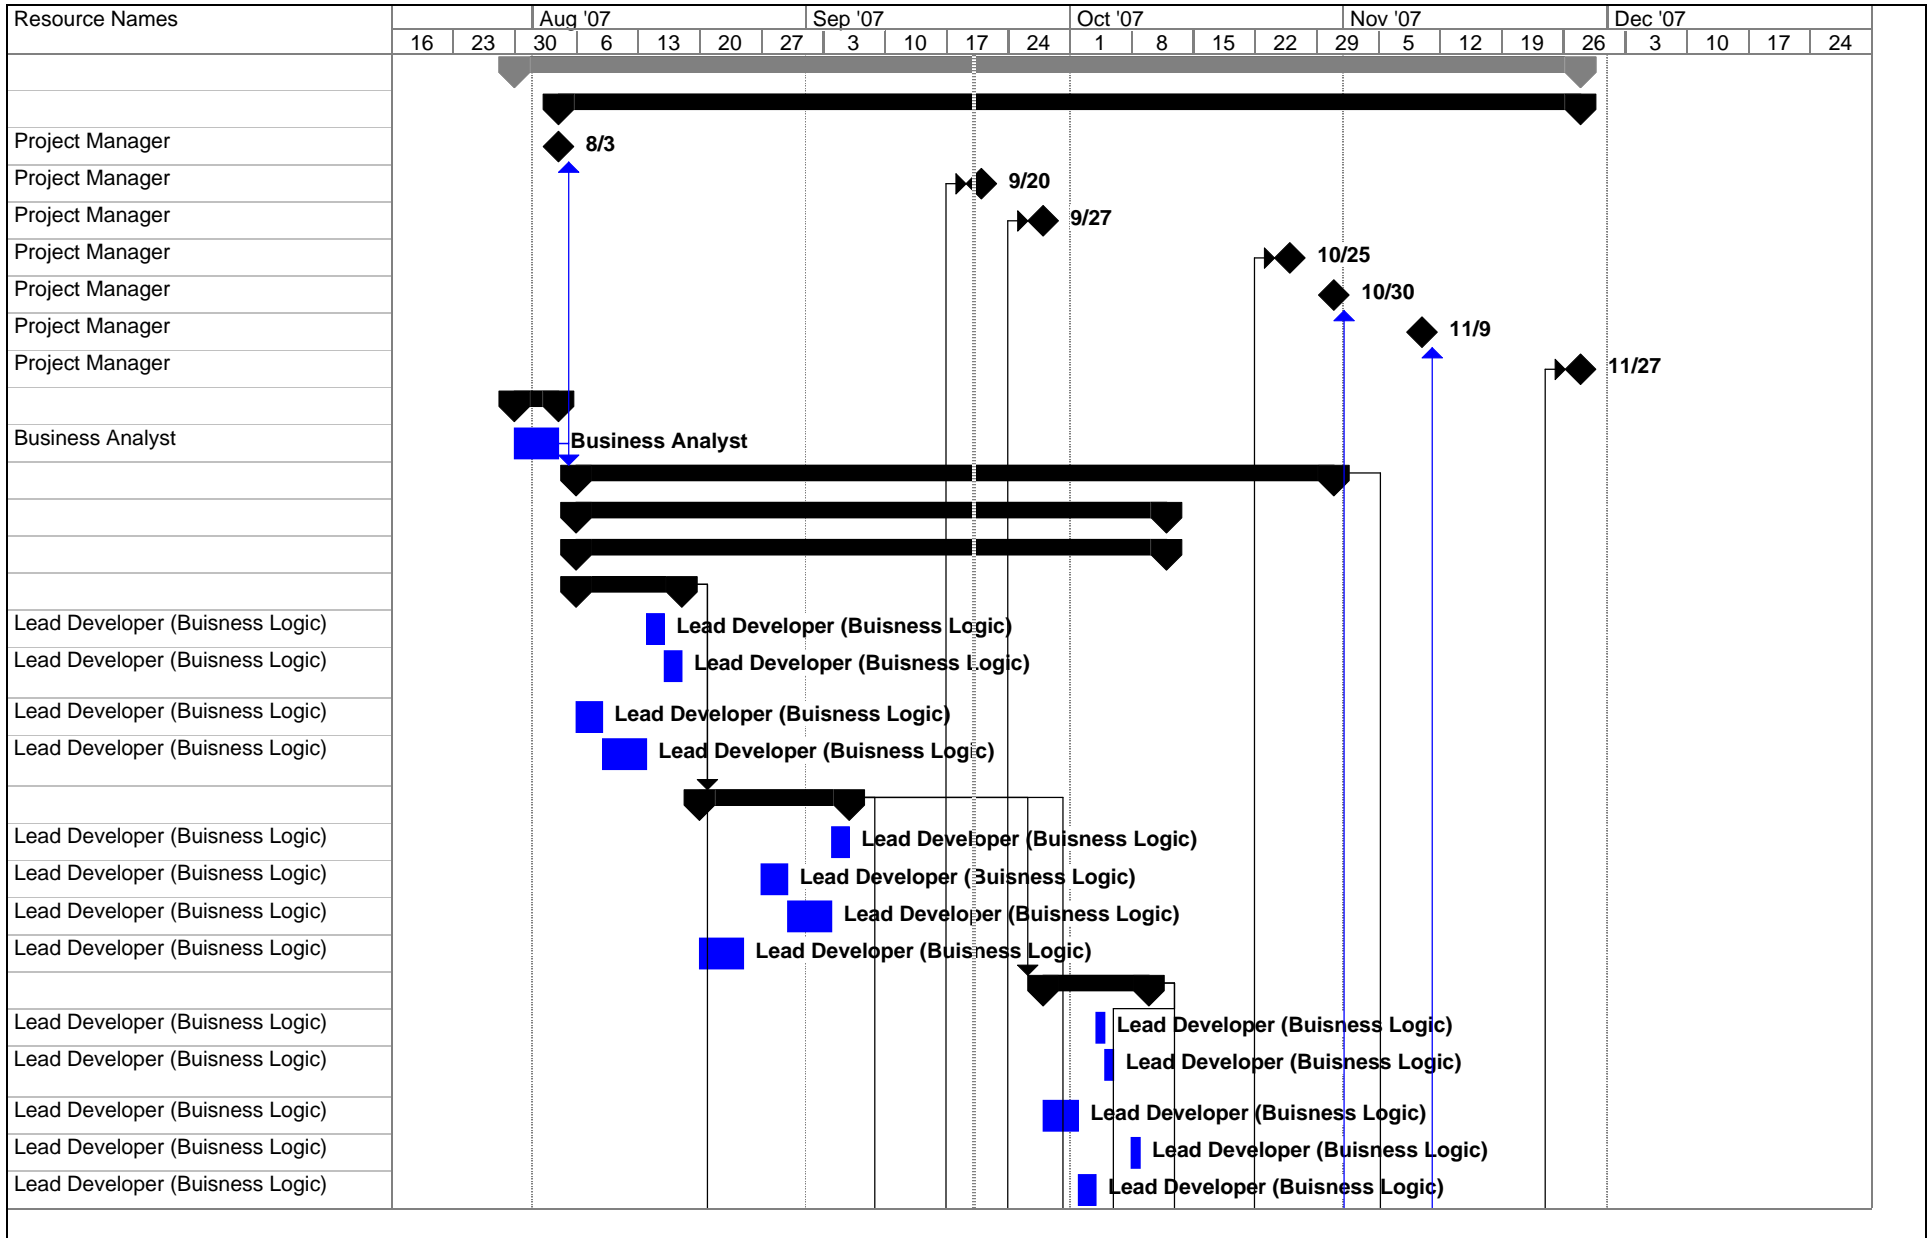

Project: WBS [PMP - phase 1] Date: Thu 9/20/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

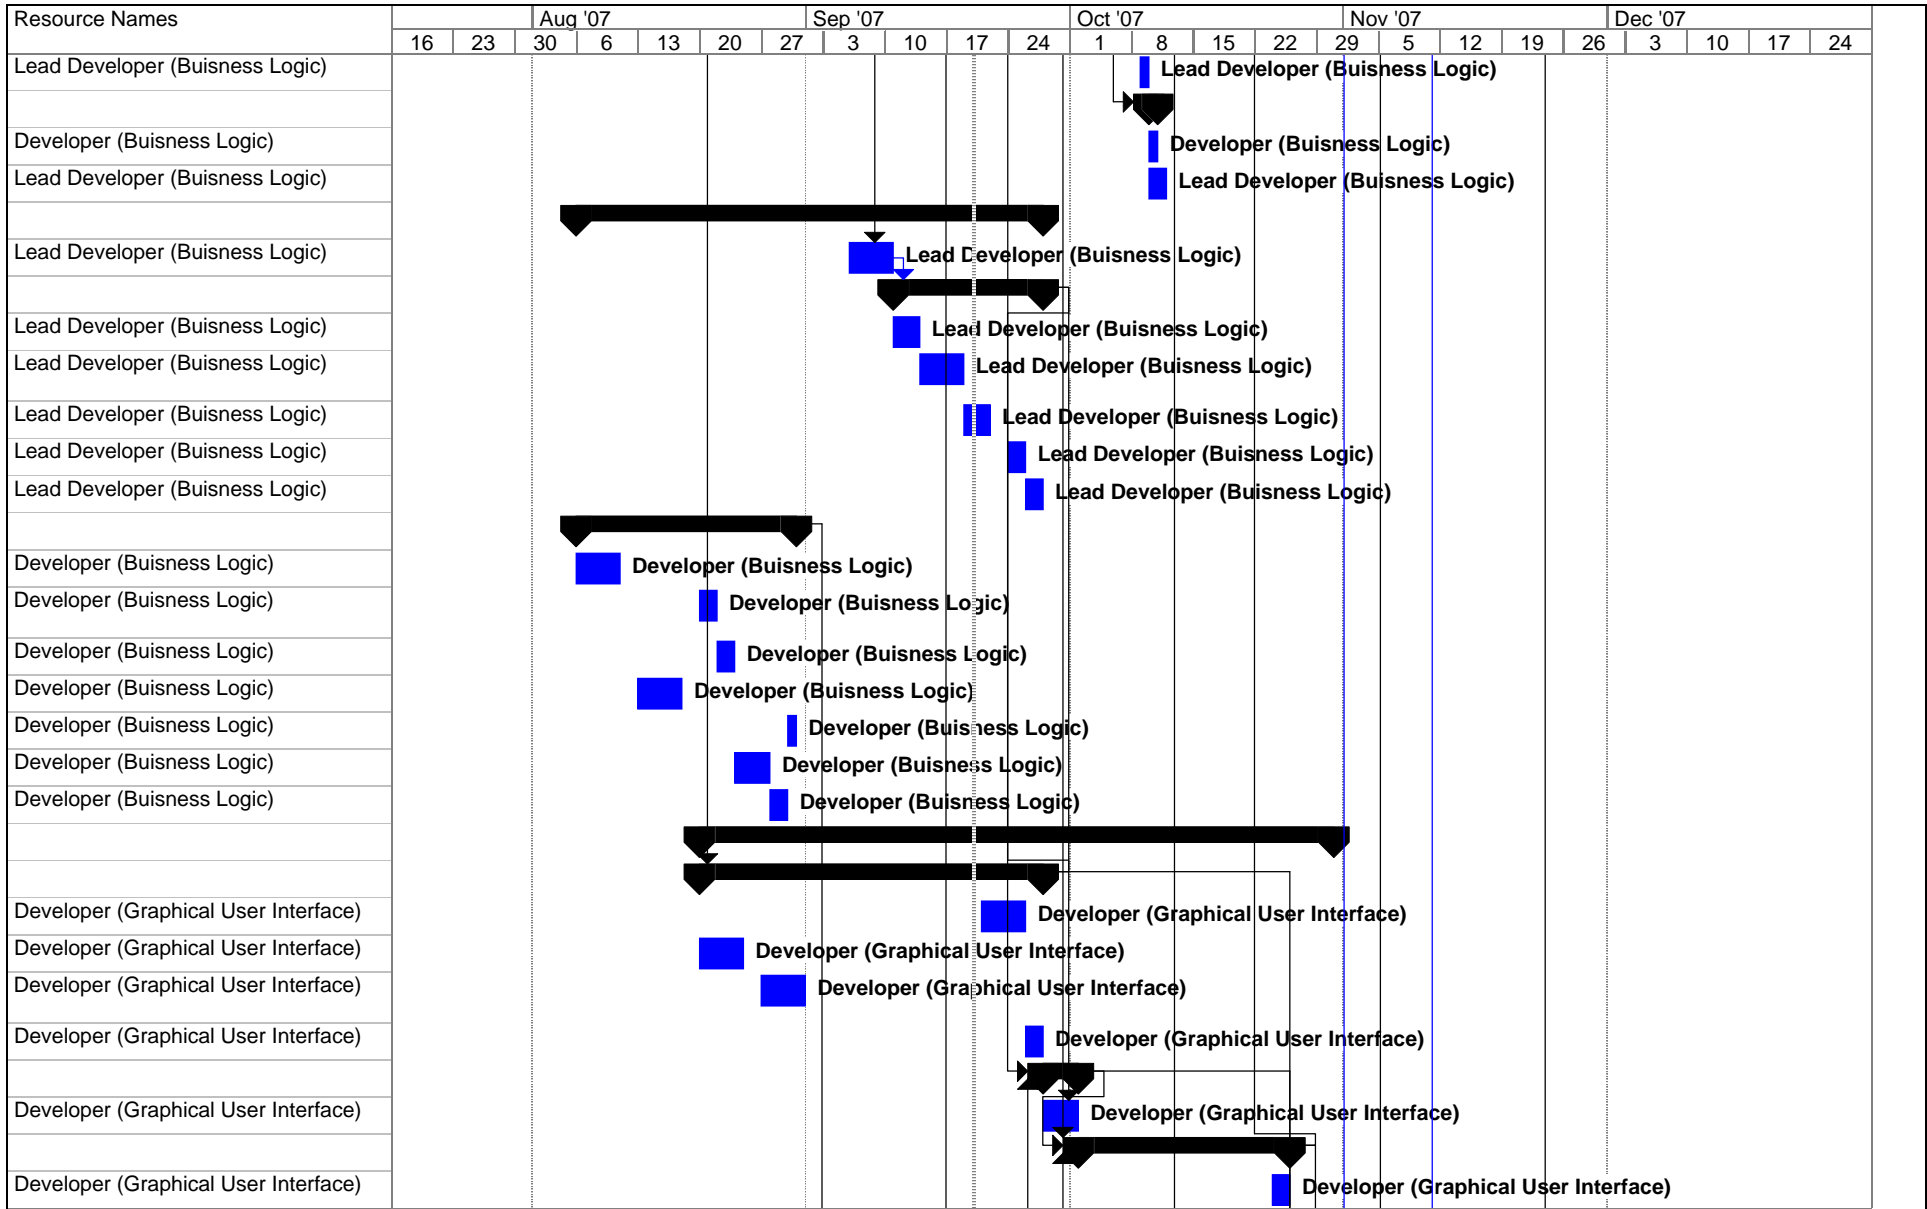



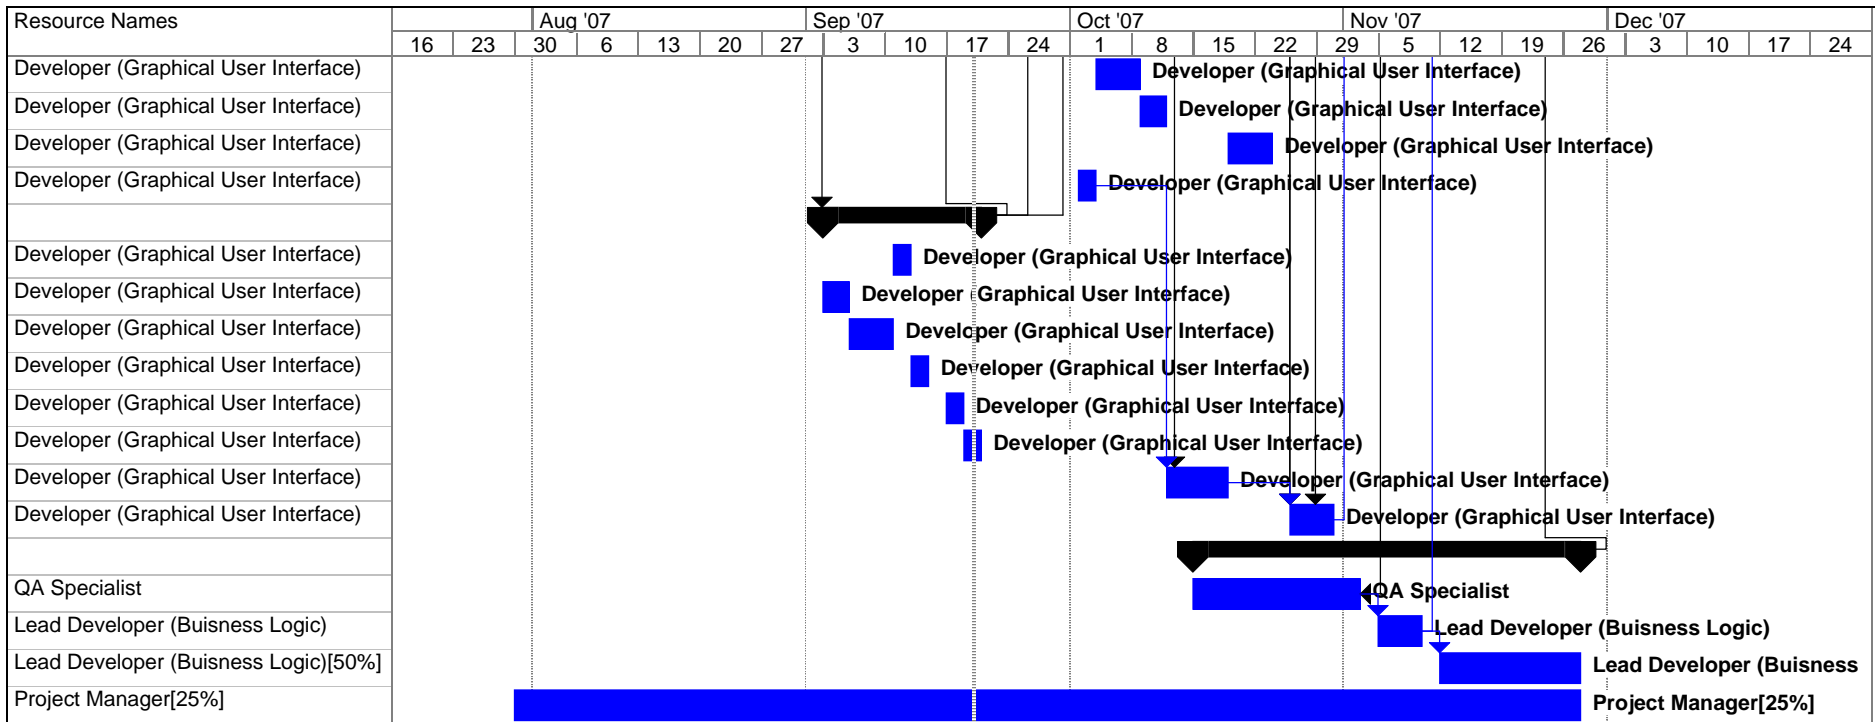






Project: WBS [PMP - phase 1] Date: Thu 9/20/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	












Project: WBS [PMP - phase 1] Date: Thu 9/20/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

Jan '08					Feb '08				Mar '08				Apr '08				May '08				Jun '08				Jul '08				A		
31	7	14	21	28	4	11	18	25	3	10	17	24	31	7	14	21	28	5	12	19	26	2	9	16	23	30	7	14	21	28	

Project: WBS [PMP - phase 1] Date: Thu 9/20/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	











Jan '08					Feb '08				Mar '08				Apr '08				May '08				Jun '08				Jul '08				A		
31	7	14	21	28	4	11	18	25	3	10	17	24	31	7	14	21	28	5	12	19	26	2	9	16	23	30	7	14	21	28	

Project: WBS [PMP - phase 1] Date: Thu 9/20/07	Task 	Milestone 	External Tasks 
	Split 	Summary 	External Milestone 
	Progress 	Project Summary 	Deadline 

Jan '08				Feb '08				Mar '08				Apr '08				May '08				Jun '08				Jul '08				A			
31	7	14	21	28	4	11	18	25	3	10	17	24	31	7	14	21	28	5	12	19	26	2	9	16	23	30	7	14	21	28	
Logic)[50%]																															



Project: WBS [PMP - phase 1] Date: Thu 9/20/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	
